

Fox Road to Fitzherbert Avenue – Link Road



Project Name:	Fox Road to Fitzherbert Avenue Link Road	Fortnight Ending:	27/02/2026
Project Manager:	Jack Pilet	Fortnightly Report No.	008

Fortnightly Report

SUMMARY OF LOCATION AND DESCRIPTION WORKS COMPLETED THIS FORTNIGHT



Fox Road to Fitzherbert Avenue – Link Road



**WHANGANUI
DISTRICT COUNCIL**
Te Kaunihera a Rohe o Whanganui



WORKS SUMMARY

The following bulleted list provides a summary of what has been achieved in the last fortnight.

- Construction of WW Main between WWMH7 and WWMH8.
- Construction of wastewater laterals and haunching of wastewater manholes.
- Construction of stormwater line between SWMHX and SWMHXY.
- Repair and maintenance of environmental controls.

TWO WEEK LOOKAHEAD

Over the coming fortnight, sewer and stormwater installation will progress with the wastewater expected to reach WWMH9 and continue towards WWMH10. Stormwater will continue at SWMHXY and progress towards SWMH5. A crew from Downer will be arriving on site on Monday 09th March to begin works on Watkins retaining wall. Once the variation has been approved, we will look to demolish the shed near the Fox Road end as soon as possible. We will also be looking to begin carting waste sand off site and reusing what we can.

Monday, 2 March 2026	Install Sewer Main (Loaders)	Install WWMH8 and connections
	Install Stormwater Main (Loaders)	Install SWMHXY and connections
Tuesday, 3 March 2026	Install Sewer Main (Loaders)	Install WWMH8 and connections
	Install Stormwater Main (Loaders)	Install SWMHXY and connections
Wednesday, 4 March 2026	Install Sewer Main (Loaders)	Install sewer main pipe between WWMH8 to WWMH9.
	Install Stormwater Main (Loaders)	Install SWMHXY and connections
	Install Sewer Laterals (Loaders)	Install sewer laterals in ROW
Thursday, 5 March 2026	Install Sewer Main (Loaders)	Install sewer main pipe between WWMH8 to WWMH9.
	Install Stormwater Main (Loaders)	Install stormwater main pipe between SWMHXY to SWMH5
	Install Sewer Laterals (Loaders)	Install sewer laterals in ROW
Friday, 6 March 2026	Install Sewer Main (Loaders)	Install sewer main pipe between WWMH8 to WWMH9.
	Install Stormwater Main (Loaders)	Install stormwater main pipe between SWMHXY to SWMH5
	Install Sewer Laterals (Loaders)	Install sewer lateral to 130 Mosston Road boundary
Saturday, 7 March 2026		
Sunday, 8 March 2026		
Monday, 9 March 2026	Construct Retaining Wall	Construct Watkins retaining wall
	Install Sewer Main (Loaders)	Install sewer main pipe between WWMH8 to WWMH9.
	Install Stormwater Main (Loaders)	Install stormwater main pipe between SWMHXY to SWMH5
Tuesday, 10 March 2026	Construct Retaining Wall	Construct Watkins retaining wall
	Install Sewer Main (Loaders)	Install WWMH9 and connections.
	Install Stormwater Main (Loaders)	Install stormwater main pipe between SWMHXY to SWMH5
Wednesday, 11 March 2026	Construct Retaining Wall	Construct Watkins retaining wall
	Install Sewer Main (Loaders)	Install WWMH9 and connections.
	Install Stormwater Main (Loaders)	Install stormwater main pipe between SWMHXY to SWMH5
	Install Sewer Main (Loaders)	Testing and inspection of sewer main, Portion A.
Thursday, 12 March 2026	Construct Retaining Wall	Construct Watkins retaining wall
	Install Sewer Main (Loaders)	Install WWMH9 and connections.
	Install Stormwater Main (Loaders)	Install SWMH6 and connections.
	Install Sewer Main (Loaders)	Testing and inspection of sewer main, Portion A.
Friday, 13 March 2026	Fill at Fox Road end	Import sand / reuse trench sand to complete filling operations at Fox Road end
	Construct Retaining Wall	Construct Watkins retaining wall
	Install Sewer Main (Loaders)	Install WWMH9 and connections.
	Install Stormwater Main (Loaders)	Install SWMH6 and connections.
	Demolish shed	Demolish and remove old shed from Fox Road end
130 Mosston Road Works	Level and grass 130 Mosston Road	

NOISE AND DUST


- Sprinklers are in place and working on a timer system.
- Construction noise is being monitored. LAeq (continuous noise) recorded for the fortnight was within the NZS 6803 limits. Lamax (impulsive) noise recorded was also within the NZS 6803 limits.

Fox Road to Fitzherbert Avenue – Link Road



WEATHER REPORT

Weather over the past fortnight was mostly warm days with varying wind. Wind direction was a mix of westerlies, easterlies and southerlies. Over the night of Sunday 15th February and during the day of the 16th, Whanganui experienced a minor weather event. Wind reached gusts of 68km/h and rainfall peaked at an intensity of 10.8mm/h. There was little to no rain for the remainder of the fortnight. The fortnightly weather report from the site weather station is shown below.

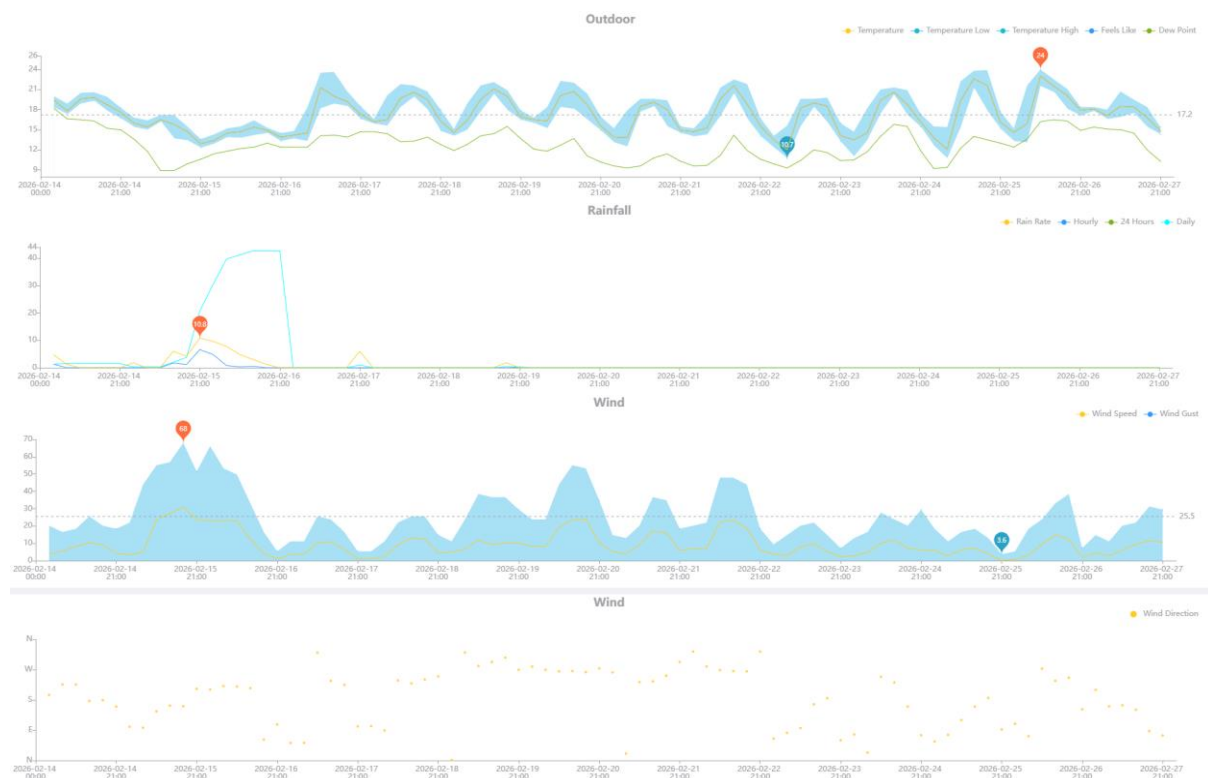

Fox Road to Fitzherbert Avenue – Link Road



WHANGANUI
DISTRICT COUNCIL
Te Kaunihera a Rohe o Whanganui

Downer
Relationships creating success

SITE PHOTOGRAPHS



Figure 1 : Installing SW pipe between SWMH4 and SWMHXY.



Figure 2 : Installing SWMHXY.

Fox Road to Fitzherbert Avenue – Link Road



Figure 3 : Dewatering along WW line.



Figure 4 : Installing WW main between WWMH7a and WWMH8.

Fox Road to Fitzherbert Avenue – Link Road



Figure 5 : SRP forebay lined with polythene.



Figure 6 : Polythene-lined SRP forebay filled with water.

Fox Road to Fitzherbert Avenue – Link Road



Figure 7 : Ground water and organic material encountered in the WW line excavation.



Figure 8 : WW works, looking north at WWMH7a.

Fox Road to Fitzherbert Avenue – Link Road



WHANGANUI
DISTRICT COUNCIL
Te Kaunihera a Rohe o Whanganui

Downer
Relationships creating success



Figure 9 : Site looking north from WWMH6.



Figure 10 : Site looking south from SWMH4.
